MISSION STATEMENT: INCREASE THE AVAILABILITY OF CAREER AND TECHNICAL EDUCATION AND TRAINING FOR HIGH SCHOOL STUDENTS AND INCUMBENT WORKERS THROUGHOUT THE BAKKEN REGION.

VISION STATEMENT: PROVIDE IN-DEMAND TRAINING OPPORTUNITIES THAT ARE RESPONSIVE TO THE NEEDS OF OUR REGION'S WORKFORCE THROUGH COLLABORATIVE PARTNERSHIPS WITH SECONDARY EDUCATION, POST-SECONDARY EDUCATION/TRAINING, AND LOCAL EMPLOYERS.

VALUES STATEMENT: PROMOTE COLLABORATION AND COMMUNICATION WITH COMMUNITY AND WORKFORCE PARTNERS TO ENSURE FLEXIBILITY AND ADAPTABILITY WITH A CHANGING ECONOMY AND APPLICABLE EMPLOYMENT SKILLS. PROVIDE RESOURCES TO PROMOTE COMMUNITY AND REGIONAL ECONOMIC SUCCESS AND OVERALL QUALITY OF LIFE THROUGH ONGOING EDUCATION AND TRAINING OPPORTUNITIES.

Project Status as of September 21st, 2022

- The site was selected by the school board at the April 11th, 2022 regular school board meeting.
- Bid Package #1 Mass grading and utilities was approved by the School Board on July 7th, 2022. The final bids accepted were substantially less than budget estimates.
- Groundbreaking Ceremony was held on July 18th, 2022.
- Bid Package #2 Structural shell construction was accepted by the School Board on September 12th, 2022 with bids substantially higher than budget estimates.
- Bid Package #3 To be released by the end of
 September, 2022 to include all remaining project items.



• Timeframe for project completion remains November, 2023 with the ability to begin classes and trainings by the end of 2023 and high school classes using the facility in January, 2024.

• Current estimated timeline of construction:

	SOMETHING NSTRUCTIVE!			BAKKEN AREA SKILLS GENTER Watford Gity, ND	Number/Version Original Page number 1A Page count 1A © Primavera Systems. Inc.
Act ID	Description	Drig Early	Early	MAY JUN JUL AUG SEEP OCT NOV DEC JAN FEB MAR APR MAY JUL AUG SEEP OCT NOV OEC NOV D91682130961332027(94/11/18/25/91/68/15/22/29/96/15/21/92/93/16/17/24/51/07/14/21/28/94/11/18/25/93/16/17/24/51/07/14/21/28/94/11/18/25/93/16/17/24/51/07/14/21/28/94/11/18/25/93/16/17/24/51/07/14/21/28/94/11/18/25/93/16/17/24/51/07/14/21/28/94/11/18/25/93/16/17/24/51/07/14/21/28/94/11/18/25/93/16/17/24/51/07/14/21/28/94/11/18/25/93/16/17/24/51/07/14/21/28/94/11/18/25/93/16/17/24/51/07/14/21/28/94/11/18/25/94/11/18/25/95/12/19/26/23/06/13/20/26/13/20/26/13/20/27/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/20/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/20/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/05/15/22/29/	
		Dur Start	Finish 020	a 14223 bolog (13 20 27 04 (11 14 25 b) 163 (12 14 2 15 a) 10 (17 24 31 (0) (14 2 1 26 05 (12 14 2 15 a) (20 2 16 (12 2 15 a) (20 2 16 (12 12 15 a) (20 2 16 (12 115 a) (20 2 16 (12 12 15 a) (20 2 16 (12 15 a) (20 2 15 (1	04 11 18 25 01 08 15 22 29 05 12 19 26 04 11
Preconstructi Bid Package #1 (
	Civil Bid Package Bidding &	10 00 00000			
01090 BP1-C 01230 BP1-N		16 08JUN22 A	29JUN22 A	SP1 - Civil Bid Package Bidding & Approval SP1 - Notice to Proceed	
	(Structural, Shell)	0	07JUL22 A	OBP1 - Notice to Proceed	
	Building Shell Design Phase	45 08JUN22 A	18411022.4	BP2 - Building Shell Design Phase	
	Building Shell Bidding &	15 19AUG22 A		BP2 - Building Shell Bidding Approval	
	Code Review & Approval	10 19AUG22 A		→ bP2 - code and she bidding a Approval	
	Notice to Proceed	0	12SEP22		
Bid Package #3			TEGET EE		
01130 BP3 - A	Architectural Design Phase	74 08JUN22 A	22SEP22	BP3 - Architectural Design Phase	
01040 BP3 - B	Bidding & Approval of Final	16 22SEP22	130CT22	V BP3 - Bidding & Approval of Final GMP	
	Code Review & Approval	10 22SEP22	05OCT22	BP3 - Code Review & Approval	
01050 BP3 - N	Notice to Proceed	0	210CT22	S BP3 - Notice to Proceed	
Construction					
Earthwork			CARL COLOR DE ST		
	ement & Mobilization	11 08JUL22 A		Procurement & Mobilization	
	Grading & Temp, Roads	40 27JUL22 A	22SEP22	American Ameri American American Ame	
01240 Water U	Utility	10 21SEP22	04OCT22	💭 Water Utility	
	g Excavation	36 28SEP22	16NOV22	Building Excavation	
	& Inlet Structures	15 15MAY23 *	05JUN23	Sewer & Inlet Structures	
01720 Site Pav		60 06JUN23	30AUG23	Site Pavement	
01730 Landsca		40 28AUG23 *	23OCT23	Landscapir	ng
Future Bid Pack					
	Submital Process	80 17AUG22 A		A PEMB Submital Process	
	Iral Steel Submittal Process	45 13SEP22	14NOV22	Structural Steel Submittal Process	
	Procurement	20 13SEP22	100CT22	A Rebar Procurement	
01450 Founda		50 06OCT22	16DEC22	A Foundations	
	f Ave Temp. Below Freezing Iral Steel Lead Time	0 08NOV22 *		Start of Ave Temp. Below Freezing	
	Lead Time	90 18NOV22	29MAR23	Structural Steel Lead Time	
	Building Shell	40 13DEC22	08FEB23	PEMB Lead Time	
	nical, Electrical, Plumbing	90 09FEB23	15JUN23	A PEMB Building Shell	
	ural Steel Shell	120 23MAR23	12SEP23	V Mechanical, Electrical, P	lumbing
01680 Structur		50 30MAR23 80 12JUL23	08JUN23 01NOV23	Structural Steel Shell	
	t Closeout	15 02NOV23	22NOV23	A Finisher	s Proiect Closeout
 Early start p Early finish 		State	immary point art milestone point	Start date 015EP21 065EP22 Update Data date 065EP22 0	vision Checked Appro NF NF
Early bar Early bar Progress ba		Fir	hish milestone poin	t Pinish date 03APR24	

- Project funding and financial support
 - On January 25th, the State CTE Board awarded \$6,666,666 to the Bakken Area Skills Center as a "shovel ready" project and utilizing state funds currently available.
 - On March 14th, the State CTE Board awarded \$3,333,334 to the Bakken Area Skills Center (State allocated Federal Coronavirus Funding) Yet to be received by the State.
 - Total of \$10 million dollars provided to the project from the State of ND through the North Dakota Department of Career and Technical Education.
 - McKenzie County Commission allocated \$4 million dollars to the BASC.
 - City of Watford City waived special assessments on the site to provide taxpayer savings.
 - In-Kind donations provided with property donation by Stenehjem Holdings as well as Mammoth (Titan Energy).
 - Industry, local businesses and community service groups donated a total of \$1,862,500.00 to date.
 ONEOK provided \$1 million in pledged donation to the BASC.
 - Initial budget of \$20,833,751 has increased to \$22,260,270 due to inflationary costs impacting bids and construction. Funding gap remains to cover the differences in secured pledges and construction costs.

• Partnerships and collaborators – opportunities for stakeholder participation


INVESTMENT LEVELS

	PLATINUM \$2 million and above	GOLD \$1 million - \$1.9 million	SILVER \$100,000 - \$999,999	BRONZE \$10,000 - \$99,999
Permanent recognition on contributor wall	Organization logo in Platinum category	Organization logo in Gold category	Organization logo in Silver category	Organization name printed in Bronze category
Participate in ground breaking	Yes	Yes	\$500,000+ contributions	No
Participate in ribbon cutting	Yes	Yes	Yes	Νο
Complementary usage of one classroom/high bay	Two days per month for three years after ribbon cutting	One day per month for three years after ribbon cutting	Four days per year for three years after ribbon cutting	One day per year for three years after ribbon cutting
TV monitor display of organization's career opportunities or message	Inclusion with the most amount of air time on repeating loop	Inclusion with the second-most amount of air time on repeating loop	Inclusion with the third-most amount of air time on repeating loop	Inclusion with the fourth-most amount of air time on repeating loop

- Educational and Workforce collaborations currently in place:
 - Williston State College Memorandum of Understanding
 - Planned curriculum/dual credit/certification programs offered through BASC
 - TrainND Memorandum of Understanding
 - Focus on certifications and pathways to employment for students and adult learners through the BASC
 - University of Mary ongoing collaboration and partnership through classes and potential 2 and 2 programs through Williston State College.
 - WERC Center Western Education Regional Cooperative Center 15 regional school districts in northwest North Dakota collaborating on education services and focus on career and technical opportunities. BASC is a regional satellite site for classes and curriculum provided to regional students.
 - Corp of Discovery High Tech consortium recognized by ND CTE providing equipment and curriculum to 23 regional school districts and aligned to curriculum offerings through the regional consortium and BASC.
 - Job Service Job Service of North Dakota as committed to an employee in the BASC up to 30 hours per week during the first year the BASC is open for services.
 - Utilization of Golden Path Solutions (Compass) through support provided by ND CTE and alignment of student competencies and workforce placements.
 - Continued collaborations and support sought from other higher education institutions and to secure high quality workforce preparation pathways and retraining certifications.

• The organizational reach and impact opportunities involving K-12 education and students potentially impacted by services provided through WERC and the BASC


TENTATIVE PARTNERS IN THE REGIONAL EFFORTS OF THE BAKKEN AREA SKILLS CENTER

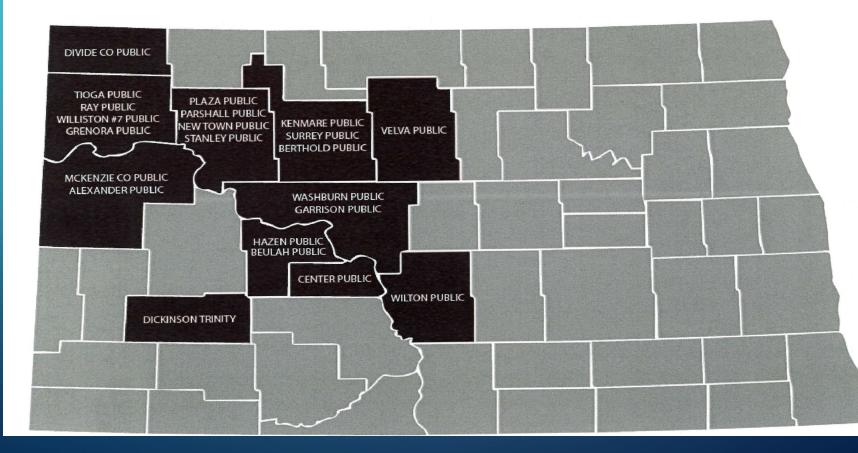

 The facility will be approximately 40,000 square feet with contingencies for expansion in the future. The building will provide high bay, multi-purpose shops with initial focus on building trades, auto/diesel mechanics, welding, and automation/IT workspace. Each shop space has its own classroom for instruction to coincide with the hands-on shop experience. The facility will also provide opportunities for mobile trailers to be utilized for outlying areas and to expand curriculum options across the region. The building will accommodate larger meetings, presentations, or trainings on a variety of levels.

PROPOSED PROGRAMMING

BASC DESIGNATED SPACES & POTENTIAL MOBILE TRAILERS

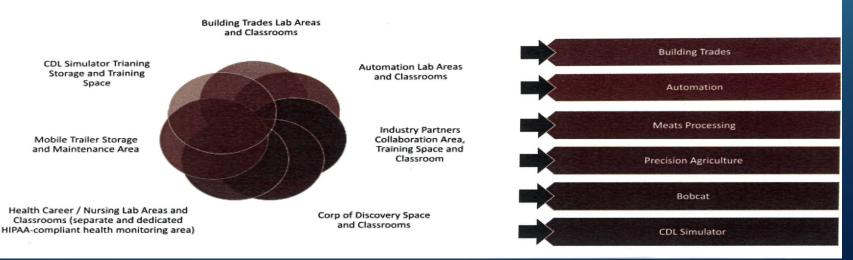

- Workforce Skills Initiative transition to advisory committee status to provide continual and ongoing input into programming and curriculum development to reflect changes in the workforce and innovation in the various content areas.
- Connection of student learning competencies and workforce preparation; utilizing resources and regional staff as well as workforce collaboration to provide meaningful workforce experiences, apprenticeships, and align students/employers for success.
- 4 c's Communication, collaboration, critical thinking, and creativity as keys to success for all stakeholders.



• Current building floor plan and renderings:



• Current building floor plan and renderings:



Current building floor plan and renderings:



• Current building floor plan and renderings:



• Current building floor plan and renderings:





Entrance





• Contact Information:

• Dr. Steven Holen

McKenzie County Public School District #1

701-444-3626

sholen@Watford-city.k12.nd.us

• Daniel Stenberg

McKenzie County Economic Development

701-444-7419

dstenberg@co.mckenzie.nd.us

• Website – https://www.watford-city.k12.nd.us/bakkenskills
